

Scrum II — the events, the artifacts, the Definition of Done

DIG 123 · Agile Methodologies for Innovation · Class 4 · Monday, October 12, 2026 · Sprint 1 starts today

Cyber.SoHo Educational Hub · From the Industry to the Classroom — Building the IT's Future, Today and Together !
Legal Notice, Terms of Use and Acceptable Use Policy: https://cyber-soho.github.io/prevmon/00.01.%20cyber.soho%20-%20legal.html
Scrum Guide 2020 wording © Ken Schwaber and Jeff Sutherland, CC BY-SA 4.0 · Team Menu and its members are fictional

The hour, minute by minute

Time	Part
0:00–0:02	Check-in
0:02–0:12	Lesson 1 · The Sprint and Sprint Planning
0:12–0:17	Activity 1 · Visualization: a Sprint on a timeline
0:17–0:27	Lesson 2 · The Daily Scrum and the Sprint Review
0:27–0:32	Activity 2 · Mini-exercise: a 3-minute Daily Scrum
0:32–0:42	Lesson 3 · The Sprint Retrospective and the three artifacts
0:42–0:47	Activity 3 · Flash-cards ×6: artifacts and commitments
0:47–0:57	Lesson 4 · The Definition of Done
0:57–1:00	Activity 4 · Fun-quiz ×3 "done or not done?" + zen-break

Today you will be able to

- Define the Sprint and state the four rules that hold while it runs, who may cancel it, and why shorter Sprints lower risk.
- Describe Sprint Planning — why, what, how — and its output, the Sprint Backlog; compute a capacity in hours and select items within a capacity in points.
- State the purpose, time-box, participants and output of the Daily Scrum, the Sprint Review and the Sprint Retrospective, and say which artifact each one inspects and adapts.
- Define the three artifacts and pair each one with its commitment: Product Goal, Sprint Goal, Definition of Done.
- Define the DoD (Definition of Done), distinguish it from acceptance criteria, and write five observable checks for your own product.
- Syllabus Topic 1 · Learning outcomes LO 1, LO 3, LO 4

Where we are: Sprint 1 starts today

- Last week: the people of Scrum — three accountabilities, empiricism, five values
- Today: the five events and the three artifacts, and the commitment that decides when work is finished
- Sprint 1: Monday, October 12 → Sunday, October 25 (two weeks)
- No new lab this Monday: the Team Studio is a guided practice of the events on your own product
- Everything you write today is the input of Lab 03 (Sprint 1 Kit & User Story Set), next Monday, October 19 — feedback date Sunday, October 25
- Feedback dates are not penalized; the final deadline of every lab is Sunday, December 20, 2026, 23:59



1

Lesson 1 · The Sprint and Sprint Planning

0:02 – 0:12 · then Activity 1 (0:12 – 0:17)

The Sprint: the container of everything else

- Scrum Guide 2020: Sprints are "fixed length events of one month or less to create consistency"
- Rule 1 — fixed length: decided before the Sprint starts, not changed while it runs
- Rule 2 — one month or less: a maximum, not a minimum; most teams choose one or two weeks
- Rule 3 — consecutive: "a new Sprint starts immediately after the conclusion of the previous Sprint"
- All the work needed to reach the Product Goal happens inside Sprints — no "Sprint 0", no separate testing Sprint
- This course: two-week Sprints · Sprint 1 = Oct 12 → Oct 25 · Sprint 2 starts Oct 26

Why a shorter Sprint lowers risk

- A Sprint is a period of work on assumptions that are checked only at its end
- Guide: when the horizon is too long, "the Sprint Goal may become invalid, complexity may rise, and risk may increase"
- Shorter Sprints "generate more learning cycles and limit risk of cost and effort to a smaller time frame"
- Same logic as last week's empirical loop: at most one Sprint of work can rest on a wrong assumption
- Two weeks = at most ten working days built on an error before the Review exposes it

Four rules that hold while the Sprint runs (1/2)

Rule (Scrum Guide 2020)	What it means for your team
"No changes are made that would endanger the Sprint Goal."	The Sprint Goal is the one thing that does not move. A request that would make the goal unreachable waits for the next Sprint.
"Quality does not decrease."	The checks in your DoD (Definition of Done) are never skipped to finish faster (Lesson 4).
"The Product Backlog is refined as needed."	The Product Owner keeps improving the items that are not in the Sprint, so that they are ready for the next Sprint Planning.
"Scope may be clarified and renegotiated with the Product Owner as more is learned."	The amount of work may change — for example, one item is dropped when it turns out larger than expected — as long as the Sprint Goal still holds, and only in agreement with the Product Owner.



Scope versus goal, and cancelling a Sprint (2/2)

- Scope = the list of Product Backlog items in the Sprint → may be renegotiated with the Product Owner
- Goal = the single objective those items serve → protected for the whole Sprint
- Team Menu, day eight: the French version is bigger than estimated → it leaves the Sprint; the Sprint Goal still holds in English
- Cancelling: "a Sprint could be cancelled if the Sprint Goal becomes obsolete" — only the Product Owner has that authority
- A difficult Sprint is not a reason to cancel; a goal that no longer has value is
- Forecasting aids (burn-downs, burn-ups, cumulative flows) "do not replace the importance of empiricism"

Sprint Planning: why, what, how

Topic	Who leads	What is decided
Why is this Sprint valuable?	The Product Owner "proposes how the product could increase its value and utility in the current Sprint"; then the whole Scrum Team collaborates to define the Sprint Goal.	One sentence: the objective of the Sprint. Written during Sprint Planning and added to the Sprint Backlog.
What can be Done this Sprint?	The Developers, "through discussion with the Product Owner", select items from the Product Backlog. The Developers are responsible for sizing.	The list of Product Backlog items for the Sprint. Items that "can be Done by the Scrum Team within one Sprint are deemed ready for selection".
How will the chosen work get done?	The Developers alone — "nobody else tells them how".	A plan: "often done by decomposing Product Backlog items into smaller work items of one day or less".


Capacity, the Sprint Goal and the Sprint Backlog

- Guide: "The more the Developers know about their past performance, their upcoming capacity, and their Definition of Done, the more confident they will be in their Sprint forecasts"
- Capacity in hours: members × hours per day × working days − time of the events
- Capacity in story points: against the velocity of past Sprints (Class 5)
- Team Menu, no past Sprint: a cautious 10 points, about 29 hours for four students
- Sprint Backlog = Sprint Goal (why) + selected items (what) + plan (how)
- Sprint Goal: "the single objective for the Sprint" — a commitment by the Developers that "provides flexibility in terms of the exact work needed to achieve it"



Diagram 1 · A two-week Sprint on a timeline

Diagram 1 · A two-week Sprint on a timeline, and the time-boxes of the five events

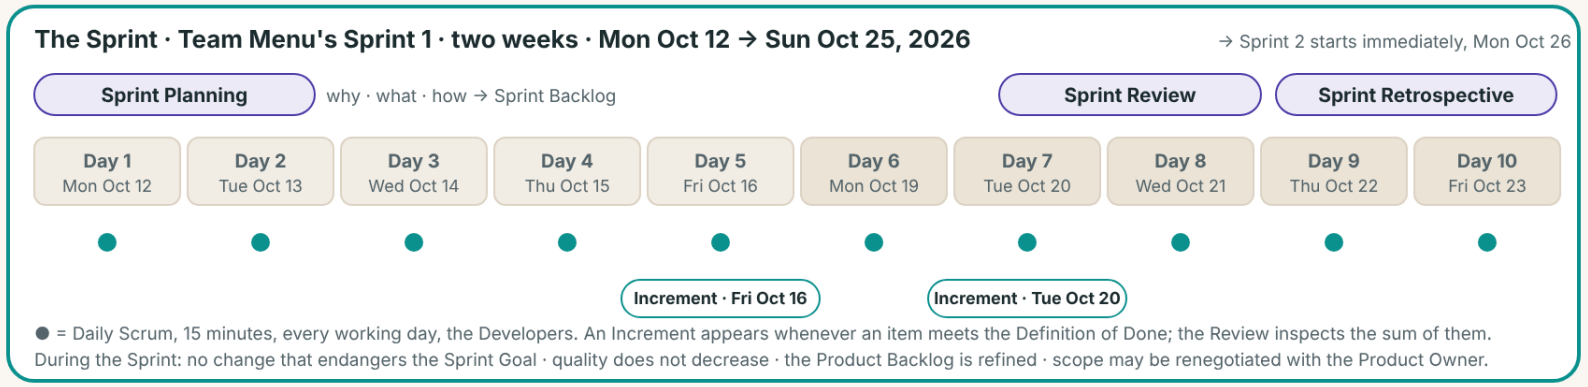

Time-boxes (Scrum Guide 2020: maxima for a one-month Sprint; usually shorter for shorter Sprints)

Event	Max time-box · one-month Sprint	Team Menu · two-week Sprint	Purpose
The Sprint	one month or less (fixed length)	2 weeks · Oct 12 → Oct 25	ideas turned into value; consistency
Sprint Planning	8 hours	20 min · Team Studio, Oct 12	why · what · how → Sprint Backlog
Daily Scrum	15 minutes	15 min max · Mon/Wed/Fri 18:00, chat	inspect progress toward the Sprint Goal; adapt the plan
Sprint Review	4 hours	20 min · Sun Oct 25, online	inspect the outcome; adapt the Product Backlog
Sprint Retrospective	3 hours	10 min · Sun Oct 25, after the Review	plan ways to increase quality and effectiveness

DIG 123 · Class 4 · Cyber.SoHo © 2026 · Scrum Guide 2020 wording © Schwaber & Sutherland, CC BY-SA 4.0


Activity 1 · Visualization — a Sprint on a timeline (5 min)

- Blank timeline handout (Diagram 1b) or two weeks of working days on paper
- Place: Sprint Planning · the ten Daily Scrums · Sprint Review · Sprint Retrospective
- Mark where the Increment appears
- 2 min alone, without notes · 2 min with your neighbour: point at the day on which each of the four rules could be tested · 1 min: two volunteers read theirs aloud
- Answer key: Diagram 1 — open it only when the time is up

Real-life example · Team Menu's Sprint 1 Planning (1/2)

Order	Product Backlog item	Size (points)	Running total	In Sprint 1?
1	3 hot meals + allergens	3	3	yes
2	Show sesame on every dish	1	4	yes
3	Icons readable on a phone	2	6	yes
4	French version	3	9	yes
5	Filter: no peanuts / tree nuts	5	14	no — does not fit (9 + 5 > 10)
6	Weekly menu view	3	—	no
7	Daily-specials banner	2	—	no
8	Kitchen edits an entry in under 2 minutes	5	—	no
9	Dark mode	2	—	no

Real-life example · the plan and the four rules (2/2)

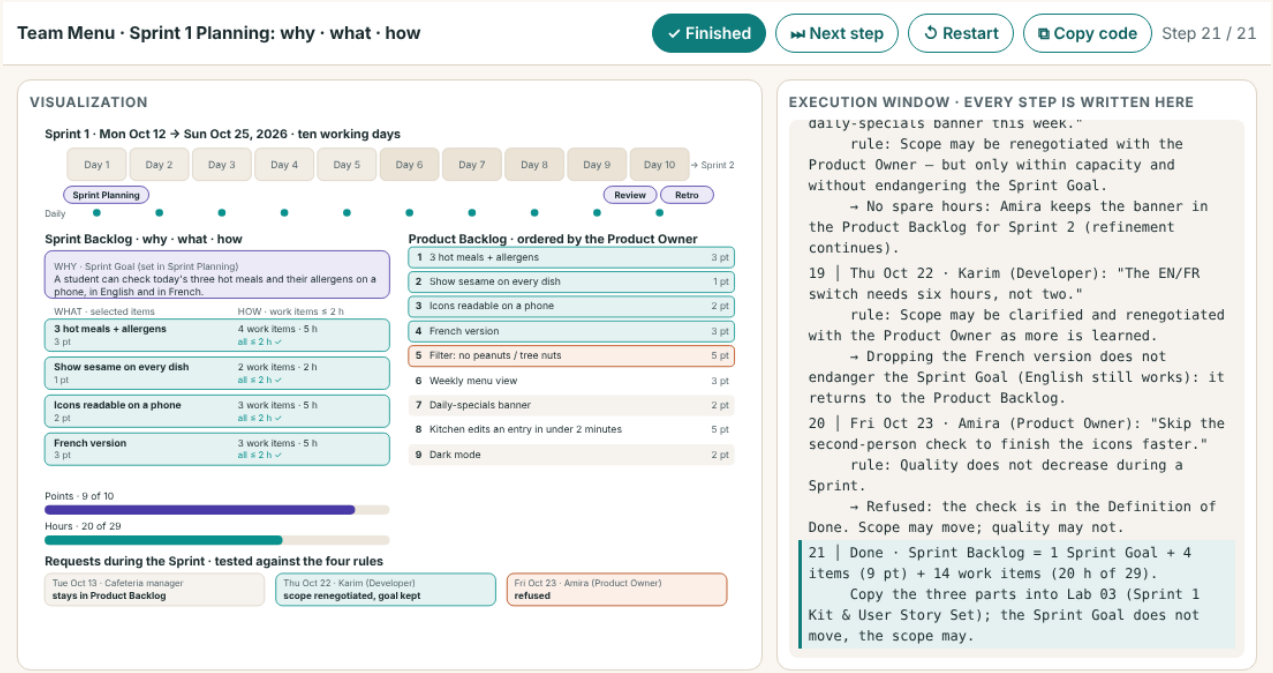

- How: fourteen work items of two hours or less = 20 hours of 29 available (margin 9 h)
- Tue Oct 13 — the manager's banner: no spare hours → stays in the Product Backlog for Sprint 2
- Wed Oct 21 — the EN/FR switch needs 6 h, not 2 → scope renegotiated with the Product Owner; Sprint Goal kept
- Fri Oct 23 — "skip the second check" → refused: quality does not decrease
- Example 1 in the companion ZIP replays every step (Start / Pause / Next step)

2

Lesson 2 · The Daily Scrum and the Sprint Review

0:17 – 0:27 · then Activity 2 (0:27 – 0:32)

The Daily Scrum: fifteen minutes, every working day

- Purpose (Guide): "inspect progress toward the Sprint Goal and adapt the Sprint Backlog as necessary, adjusting the upcoming planned work"
- Time-box: 15 minutes · "held at the same time and place every working day of the Sprint"
- Who: the Developers · the Product Owner and the Scrum Master take part as Developers when they work on Sprint Backlog items
- Output: "an actionable plan for the next day of work" — and the impediments the Scrum Master causes to be removed
- What is inspected: progress toward the Sprint Goal — not the progress of each person



Daily Scrum: format, anti-patterns, and our course adaptation

- Format is free: "The Developers can select whatever structure and techniques they want, as long as their Daily Scrum focuses on progress toward the Sprint Goal"
- The three questions (since the last / until the next / what blocks me) come from the 2013–2017 Guides — one option, not a rule
- Effects (Guide): improve communications, identify impediments, promote quick decision-making, eliminate the need for other meetings
- Anti-pattern 1 — the status report to a manager · Anti-pattern 2 — the problem-solving session while the others wait
- Course adaptation: an asynchronous Daily Scrum — a fixed-time message thread answered within 15 minutes — counts, three times a week (Team Menu: Mon/Wed/Fri 18:00)
- Say in your lab that this is an adaptation: companies hold it every working day

The Sprint Review: inspecting the outcome with the stakeholders

- Purpose (Guide): "inspect the outcome of the Sprint and determine future adaptations"
- Who: the Scrum Team and the key stakeholders (for Team Menu: the cafeteria manager, two students with allergies)
- What is inspected: the outcome — the Increment, what actually meets the Definition of Done, and its effect for users (outcome ≠ output)
- What is adapted: "the Product Backlog may also be adjusted to meet new opportunities" — the Product Owner leaves with a changed backlog
- Second-to-last event · time-box 4 hours for a one-month Sprint (about 2 h for two weeks; 20 min for Team Menu)



A working session, not a presentation


- Guide: "The Sprint Review is a working session and the Scrum Team should avoid limiting it to a presentation"
- Demonstration = showing the Increment · working session = stakeholders use it, ask, and change the backlog with the Product Owner
- An item that does not meet the Definition of Done "cannot be released or even presented at the Sprint Review"
- The Review "should never be considered a gate to releasing value" — an Increment may be delivered before the Review
- The Product Owner does not discover the Increment at the Review: acceptance happens during the Sprint, item by item

Two loops of different sizes

	Daily Scrum	Sprint Review
Frequency	Every working day	Once per Sprint, second-to-last event
Time-box	15 minutes	4 hours for a one-month Sprint (shorter for shorter Sprints)
Who	The Developers (Product Owner and Scrum Master only when they build)	The Scrum Team and key stakeholders
Inspects	Progress toward the Sprint Goal	The outcome of the Sprint — the Increment — and progress toward the Product Goal
Adapts	The Sprint Backlog (the plan for the next day)	The Product Backlog (what to do next)
Output	An actionable plan for the next day of work	Decisions on what to do next; an adjusted Product Backlog

Diagram 2 · Two inspection loops: every day, and every Sprint

Diagram 2 · Two inspection loops: every working day (Daily Scrum) and every Sprint (Sprint Review)

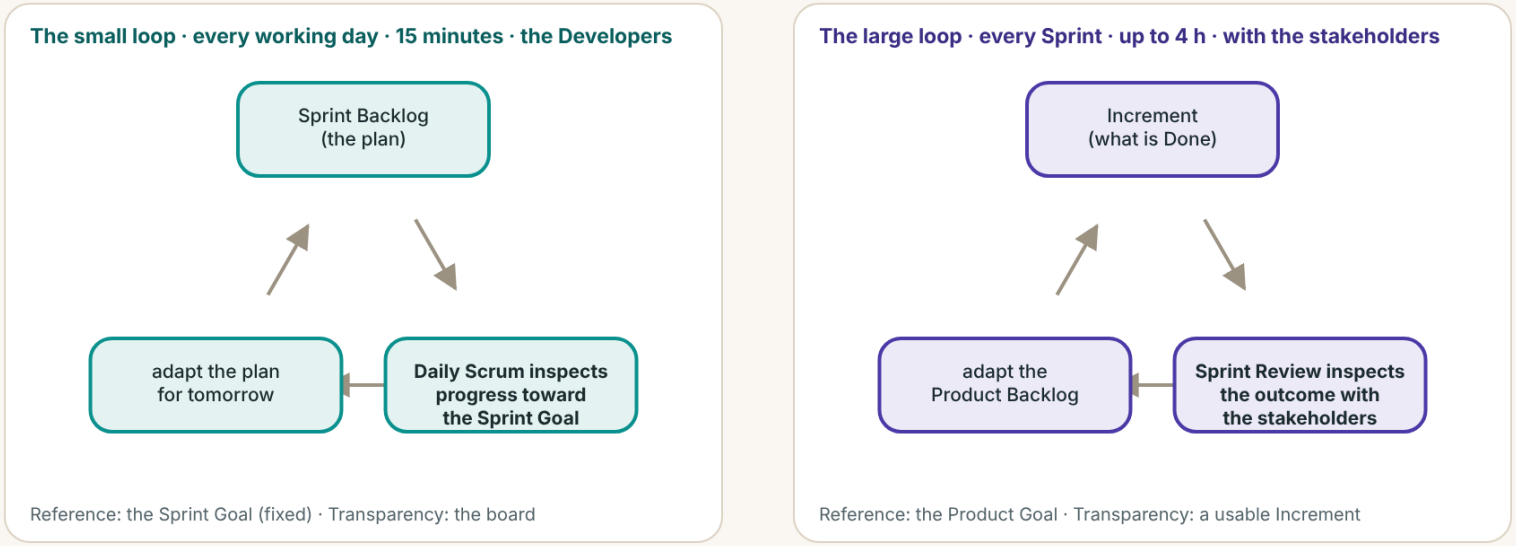

The third loop · Sprint Retrospective · every Sprint · the Scrum Team inspects the way of working and the Definition of Done → adapts the process (Lesson 3)
Three loops, one pattern: transparency → inspection → adaptation (Class 3). What differs is the artifact inspected, the reference used, and who is in the room.

Team Menu's three asynchronous Daily Scrums (first week of Sprint 1)

Date	Progress toward the Sprint Goal	Impediment	Plan adapted
Mon Oct 12	Cards collected; typing started; icon licences checked	none	unchanged
Wed Oct 14	Three meals typed; icons chosen; sesame added	Thursday's card arrives Thu morning	check → Thu; French labels → Wed; SM asks chef for photos
Fri Oct 16	Meals + sesame checked, on the test link; icons on 2 of 3	Karim's laptop at repair	Amira takes the icons; Karim reviews French on phone

DIG 123 · Class 4 · Cyber.SoHo © 2026 · Scrum Guide 2020 wording © Schwaber & Sutherland, CC BY-SA 4.0

Activity 2 · Mini-exercise — a 3-minute Daily Scrum (5 min)

- In your team, standing; today's Scrum Master holds a timer: three minutes
- Each member, 40 seconds at most: what I did since Monday for our product · what I will do before Wednesday · what blocks me
- The Scrum Master writes down every impediment and nothing else
- When the timer rings, stop — even mid-sentence
- 1 min debrief in the team: finished within three minutes? which answer was a status report? which impediment was noted? · 1 min: two teams tell the class what was hard


Real-life example · Team Menu's Daily Scrum log (1/2)

Date	Progress toward the Sprint Goal	Impediment	Plan adapted for the next day
Mon Oct 12	Recipe cards collected; typing of the three meals started (Noah). Icons: licence check started (Karim).	None.	Unchanged: Tue = typing; Wed = second-person check.
Wed Oct 14	Three meals typed. Icons chosen. Sesame added to the list.	The kitchen changed Thursday's meal; the card arrives Thursday morning only.	Second-person check moved from Wed to Thu evening; Sofia starts the French labels on Wed instead. Noah (Scrum Master) asks the head chef for same-day photos of changed cards.
Fri Oct 16	Meals and sesame checked and published on the test link. Icons added to two of three meals.	Karim's laptop is at repair until Monday; the icon work item is blocked.	Amira takes the third meal's icons on Saturday; Karim reviews the French on his phone. Sprint Goal still reachable.

Real-life example · the Sprint 1 Review, Sunday, October 25 (2/2)

Feedback (who)	Decision (Product Owner)	Product Backlog after the Review
"I need to know about sesame oil too, it is not always listed as sesame." (student)	New item: "Show 'contains sesame oil' separately", value 8, size 2.	Placed at #2, right after the French version.
"Students plan their week on Sunday; one day at a time is not enough." (manager)	"Weekly menu view" moves up.	From #6 to #3.
"Can the kitchen correct a wrong entry itself?" (manager)	Kept where it is: valuable, but the filter serves more students first.	#5, unchanged.
Both students used the page without help; the manager asks for a link on the cafeteria's website.	Progress toward the Product Goal confirmed; the Increment is released to the real link on Monday.	Release is not gated by the Review.

Sprint 1 burn-down: work items remaining, day by day

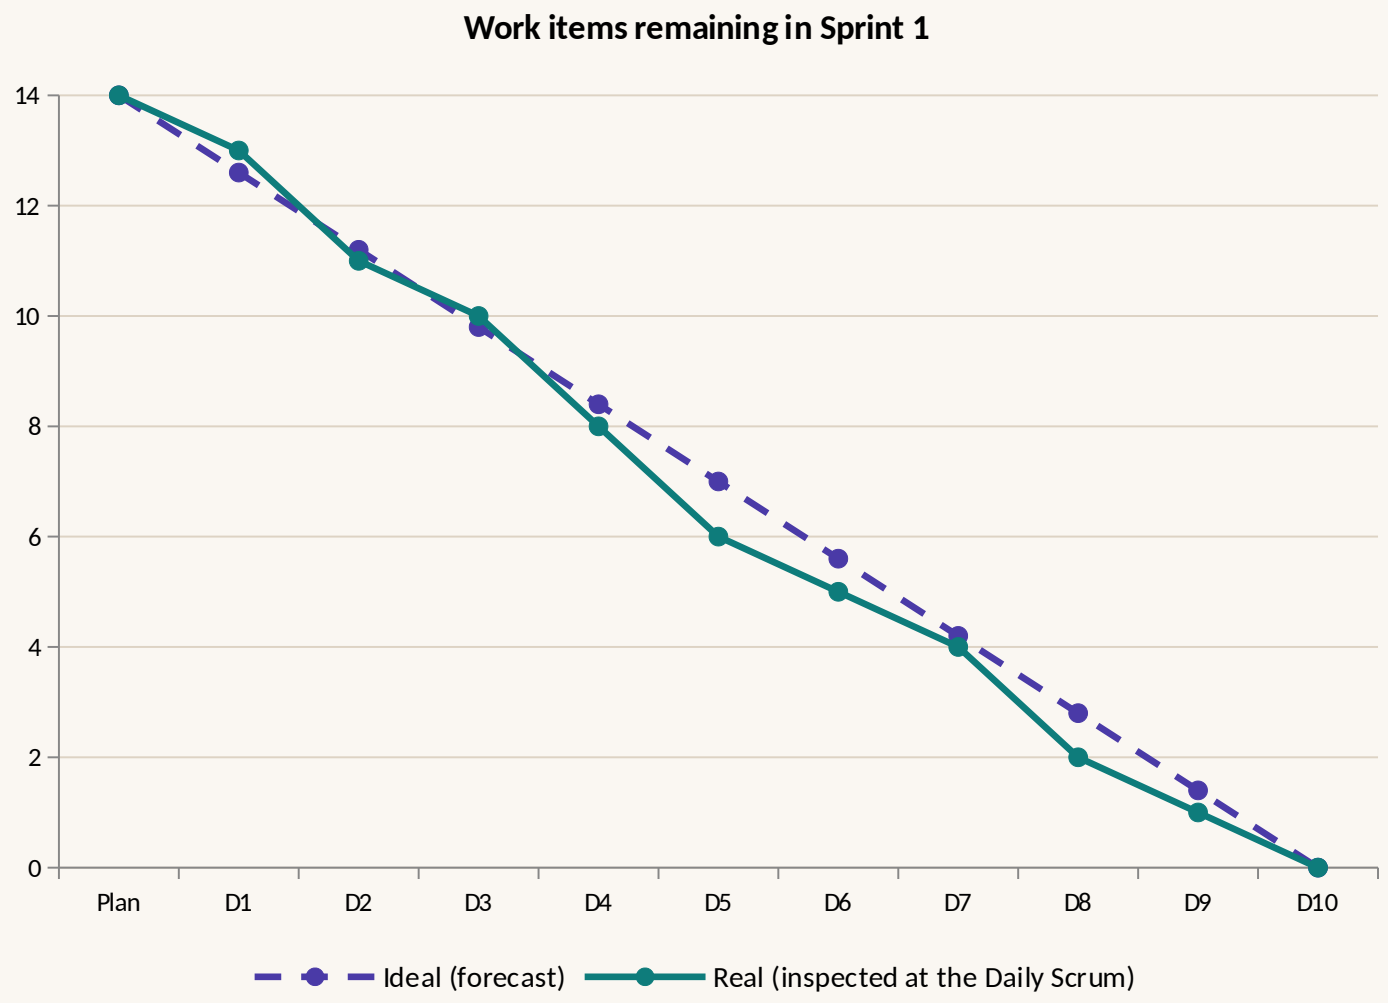

- Ideal line: 14 work items on day 0 → 0 on day 10 (1.4 per day)
- Real line: inspected at every Daily Scrum; impediments on days 3 and 5; scope renegotiated on day 8 (two work items left the Sprint with the French version)
- A forecast, not a target: the chart helps the Daily Scrum; only the Increment tells what is Done

3

Lesson 3 · The Sprint Retrospective, and the three artifacts with their commitments

0:32 – 0:42 · then Activity 3 (0:42 – 0:47)

The Sprint Retrospective: the team inspects itself

- Purpose (Guide): "to plan ways to increase quality and effectiveness"
- Inspects "individuals, interactions, processes, tools, and their Definition of Done" — the way of working, not the product
- Content: what went well · what problems · how they were (or were not) solved · the most helpful changes
- "The most impactful improvements are addressed as soon as possible. They may even be added to the Sprint Backlog for the next Sprint"
- The last event: it "concludes the Sprint" · time-box 3 hours for a one-month Sprint (10 min for Team Menu)
- Only the Scrum Team attends — no stakeholders



Retrospective formats, and three rules that make one useful

- Start / Stop / Continue — one note of each per member; group, then dot-vote
- 4Ls — liked · learned · lacked · longed for
- Mad / Sad / Glad — the same, sorted by how it felt
- Rule 1 — use data: the Daily Scrum log, the impediments, the items that missed the Definition of Done
- Rule 2 — choose one or two improvements, not ten
- Rule 3 — write each improvement with an owner and a way to measure it at the next Retrospective
- The Scrum Master facilitates, keeps the time-box, and is inspected too

The three artifacts

- Guide: "Scrum's artifacts represent work or value" — "designed to maximize transparency of key information"
- Product Backlog — "an emergent, ordered list of what is needed to improve the product"; the single source of work; owned and ordered by the Product Owner
- Sprint Backlog — Sprint Goal (why) + selected items (what) + actionable plan (how); "a plan by and for the Developers"; updated throughout the Sprint
- Increment — "a concrete stepping stone toward the Product Goal"; additive to all prior Increments; thoroughly verified; usable
- Refinement: breaking items down into smaller, more precise ones — the Developers size them; an item is ready when it can be Done within one Sprint
- "The moment a Product Backlog item meets the Definition of Done, an Increment is born" — multiple Increments per Sprint



Three artifacts, three commitments

Artifact	Commitment	What the commitment is for
Product Backlog	Product Goal	"a future state of the product which can serve as a target for the Scrum Team to plan against" — one at a time
Sprint Backlog	Sprint Goal	"the single objective for the Sprint" — a commitment by the Developers; created in Sprint Planning
Increment	Definition of Done	"a formal description of the state of the Increment when it meets the quality measures required for the product"

Diagram 3 · Artifacts, commitments, and the events that inspect and adapt them

Diagram 3 · Artifacts and their commitments, and what each event inspects and adapts

Artifact (represents work or value)	→ Commitment (reference for inspection)
Product Backlog An emergent, ordered list of what is needed to improve the product; the single source of work; refined as needed; the Developers size the items.	**Product Goal** A future state of the product that serves as a target to plan against; one Product Goal at a time; written in the Product Backlog.
Sprint Backlog Sprint Goal (why) + selected items (what) + actionable plan (how); a plan by and for the Developers; updated throughout the Sprint.	**Sprint Goal** The single objective of the Sprint; a commitment by the Developers; fixed during the Sprint; gives flexibility in the exact work.
Increment A concrete stepping stone toward the Product Goal; additive; thoroughly verified; usable; multiple Increments may be created within a Sprint.	**Definition of Done** A formal description of the state of the Increment when it meets the quality measures required for the product; an item that fails it returns to the Product Backlog.

Events × artifacts · inspects / adapts

	Product Backlog	Sprint Backlog	Increment
Sprint Planning max 8 h	**inspects** ready items; the PO proposes value	**creates** Sprint Goal, selected items, plan	**plans** against the DoD and the capacity
Daily Scrum max 15 min	—	**inspects · adapts** progress toward the Sprint Goal; plan	**builds** items reach Done during the Sprint
Sprint Review max 4 h	**adapts** new opportunities; the Product Owner	— the Sprint is over	**inspects** the outcome, with the stakeholders
Sprint Retrospective max 3 h	—	**adds** improvements → next Sprint Backlog	**inspects the DoD** and the way of working

How to read a pair: the commitment is the reference against which the artifact is inspected — the acceptable limit of Class 3 written as a goal or a standard.

Team Menu after Sprint 1

Product Backlog → Product Goal	10 ordered items; Product Goal: every student can check the allergens of every hot meal in the main cafeteria before lining up.
Sprint Backlog → Sprint Goal	Sprint Goal: today's three meals and their allergens on a phone, in English and in French — reached in English; French moved to Sprint 2.
Increment → Definition of Done	Meals + sesame + icons on the test link, used by two students; five checks, all met; the French version returned to the Product Backlog.

DIG 123 · Class 4 · Cyber.SoHo © 2026 · Scrum Guide 2020 wording © Schwaber & Sutherland, CC BY-SA 4.0

Activity 3 · Flash-cards ×6 — artifacts and commitments (5 min)

- Round 1, in order: Product Backlog → ? · Sprint Backlog → ? · Increment → ?
- Round 2, reversed: Product Goal → ? · Sprint Goal → ? · Definition of Done → ?
- Round 3, shuffled: "define it in one sentence"
- Answers: Product Goal · Sprint Goal · Definition of Done — a future state to plan against · the single objective of the Sprint · the quality measures the Increment must meet



Real-life example · Team Menu's Sprint 1 Retrospective (1/2)

Column	Note	Dots
Stop	Publishing an entry before the second-person check	4
Stop	Estimating an item without opening the page where it will be built (the EN/FR switch)	2
Start	Attaching a photo of the recipe card to every entry	1
Start	Asking the kitchen for next week's cards on Friday	1
Continue	The Daily Scrum in the chat at 18:00 — all three happened on time	0
Continue	Amira taking over a blocked work item instead of waiting	0

Real-life example · Team Menu's artifacts on one page (2/2)

Artifact	Team Menu, October 25	Commitment	Team Menu's commitment
Product Backlog	Ordered list of 10 items after the Review: French version, 'contains sesame oil', weekly menu view, filter, kitchen edits, banner, dark mode… (one page, on the board)	Product Goal	Every student can check the allergens of every hot meal in the main cafeteria before lining up.
Sprint Backlog (Sprint 1)	Sprint Goal + 4 items + 14 work items of two hours or less; updated at every Daily Scrum; the French item left on day 8	Sprint Goal	A student can check today's three hot meals and their allergens on a phone, in English and in French — reached in English; the French part moved to Sprint 2.
Increment	Three meals with allergens, sesame on every dish, icons readable on a phone — on the test link, used by two students, released to the real link on Monday	Definition of Done	The five checks of Lesson 4: in the shared folder, second-person check against the card, readable on two phones, user note updated, Product Owner accepted.

4

Lesson 4 · The Definition of Done

0:47 – 0:57 · then Activity 4 (0:57 – 1:00)

What the Definition of Done is

- Guide: "a formal description of the state of the Increment when it meets the quality measures required for the product"
- A checklist every Product Backlog item must pass before it counts as finished — the commitment of the Increment
- "The moment a Product Backlog item meets the Definition of Done, an Increment is born"
- It "creates transparency by providing everyone a shared understanding of what work was completed"
- An item that fails it "cannot be released or even presented at the Sprint Review" — it "returns to the Product Backlog"
- Organizational standard = a minimum for all teams; otherwise the Scrum Team creates one; several teams on one product share the same Definition of Done



Done, usable, and acceptance criteria

	Definition of Done	Acceptance criteria
Applies to	Every Product Backlog item of the product — the same list each time	One item — a different list for each
Answers	Is it finished to our quality standard?	Does it do what this item is meant to do?
Written by	The Scrum Team (or inherited from the organization's standard)	The Product Owner with the Developers, per item
Changed	At the Sprint Retrospective, when the team raises its standard	Per item, during refinement
Team Menu example	Second-person check against the recipe card; readable on two phones; user note updated; Product Owner accepted	"Every dish containing sesame shows the sesame label; a dish without sesame shows nothing"

Undone work and technical debt

- Acceptance criteria met + a check of the Definition of Done failed = work that looks finished and is not
- Every check passed + criteria not met = a product of high quality that does the wrong thing
- A check skipped "just this once" becomes undone work — a test not written, a note not updated — done later, under pressure, without the details
- Accumulated undone work is one source of technical debt (Class 5): a shortcut now that costs more time later
- The Guide's protection: "Quality does not decrease" during a Sprint



A sample Definition of Done for a student software product


Protects	Check (observable by a second person)
The code itself	The change is in the shared repository (version control), and a second member has reviewed it.
Behaviour	The acceptance criteria of the item are met, and the automated tests of the product pass (or, without code, the item was tested by a second member on the real device).
Users	The feature works on a phone and on a laptop; the one-page user note is updated.
Deployment	The change is on the test link (a staging or test environment), not only on one laptop.
Acceptance	The Product Owner has used it and accepted it against the acceptance criteria.
Data and rules	No personal data of anyone outside the team is stored; third-party content has a licence the team may use (Legal Notice, sections 6.7 and 14).

Writing yours: observable, realistic, shared

- Observable — a check a second person can verify by looking, using or testing ("the code is clean" is not a check)
- Realistic — a Definition of Done the team cannot meet in two weeks produces undone work, not quality: start with five checks, raise the standard at a Retrospective
- Shared — one Definition of Done for the whole team, written where everyone sees it: on the board
- Concept products: documented in the agreed template · reviewed by a second member · in the shared folder · accepted by the Product Owner
- Today's Team Studio: version 1 of your Definition of Done — five checks every item of Sprint 1 must pass
- Lab 03 asks for exactly those five checks; the Mid-Term asks you to explain them and how they changed

Diagram 4 · Two lists before an item is Done

Diagram 4 · Two lists before an item is Done: its acceptance criteria and the team's Definition of Done

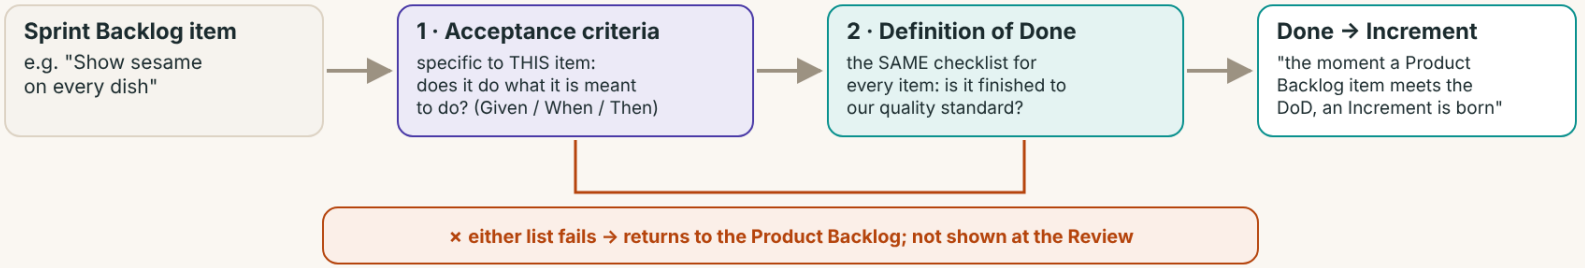

Definition of Done versus acceptance criteria

	Definition of Done	Acceptance criteria
Applies to	every item of the product — the same list each time	one item — a different list for each
Answers	is it finished to our quality standard?	does it do what this item is meant to do?
Written by	the Scrum Team (or inherited from the organization)	the Product Owner with the Developers, per item
Changed	at the Retrospective — raised, never lowered to finish	per item, during refinement

A sample Definition of Done for a student software product (adapt it, do not copy it)

- ☐ **1 · Code** — in the shared repository; reviewed by a second member
- ☐ **2 · Behaviour** — acceptance criteria met; automated tests pass (or a second member tests it)
- ☐ **3 · Users** — works on a phone and a laptop; the one-page user note is updated
- ☐ **4 · Deployment** — on the test link (staging), not only on one laptop
- ☐ **5 · Acceptance** — the Product Owner used it and accepted it against the acceptance criteria
- ☐ **6 · Data & rules** — no personal data of outsiders; third-party content with a usable licence

DIG 123 · Class 4 · Cyber.SoHo © 2026 · Scrum Guide 2020 wording © Schwaber & Sutherland, CC BY-SA 4.0

Activity 4 · Fun-quiz ×3 "done or not done?" + zen-break (3 min)

- Team Menu's five checks: in the shared folder · second-person check against the card · readable on two phones · user note updated · Product Owner accepted
- 1 — Code written, no tests, not reviewed
- 2 — The feature works on the developer's laptop only
- 3 — Documented, tested, reviewed, on the test link, Product Owner accepted
- Then 60 seconds of silence — no phones, no talking; breathe, stretch. Sprint 1 starts in the Team Studio

Real-life example · four items, five checks, Sunday, October 25

Item	Criteria met?	1 Shared	2 Check	3 Phones	4 Note	5 PO	Result
3 hot meals + allergens	yes	✓	✓ (Thu Oct 15)	✓	✓	✓ (Fri Oct 16)	Done — Increment born on Friday, October 16
Show sesame on every dish	yes	✓	✓	✓	✓	✓ (Fri Oct 16)	Done — same Increment, released together
Icons readable on a phone	yes	✓	✓ (Sat Oct 17)	✓ (Mon Oct 19)	✓	✓ (Tue Oct 20)	Done — second Increment, Tuesday, October 20
French version	no (the EN/FR switch is unfinished)	✓	×	×	×	×	Not Done — returns to the Product Backlog; not shown at the Review

Example 4 · Definition of Done checker — when is an Increment born?

Team Menu · Definition of Done: when is an Increment born? ✓ Finished | ⏭ Next step | ↻ Restart | ⧉ Copy code | Step 27 / 27

VISUALIZATION

Four items × (acceptance criteria + five checks of the Definition of Done)

	Criteria	Shared	2nd check	2 phones	User note	PO accepted	Result
3 hot meals + allergens	met	Oct 13	Oct 15	Oct 14	Oct 16	Oct 16	Done
Show sesame on every dish	met	Oct 14	Oct 15	Oct 14	Oct 16	Oct 16	Done
Icons readable on a phone	met	Oct 17	Oct 17	Oct 19	Oct 19	Oct 20	Done
French version	not met	Oct 20	×	×	×	×	not Done

When is an Increment born? · the latest of the five dates

Oct 12	Oct 13	Oct 14	Oct 15	Oct 16	Oct 19	Oct 20	Oct 21	Oct 22	Oct 23
				Increment		Increment			

Returns to the Product Backlog (not released, not shown at the Review)

French version

Version 2 · decided at the Retrospective, applies from Sprint 2

Check 2 becomes: second-person check with the photo of the card attached to the entry
Stricter and still observable; applies to every item from Sprint 2.
Items Done under version 1 stay Done — the standard may rise at a Retrospective, never fall to finish an item.

EXECUTION WINDOW · EVERY STEP IS WRITTEN HERE

```
22 | French version · check 2 (second-person check against the kitchen's recipe card) not done ✗ — undone work
23 | French version · check 3 (readable on two different phones at 320 px wide) not done ✗ — undone work
24 | French version · check 4 (one-page user note updated) not done ✗ — undone work
25 | French version · check 5 (Product Owner used it on the test link and accepted it against the acceptance criteria) not done ✗ — undone work
     → not Done (1 of 5 checks): cannot be released or presented at the Review; returns to the Product Backlog.
26 | Version 2 · check 2 → "second-person check with the photo of the card attached to the entry" · decided at the Retrospective (Lesson 3) · applies from Sprint 2 · the three Done items are not re-judged.
27 | Done · 3 of 4 items Done → 2 Increments (Oct 16 and Oct 20), both before the Review · 1 item back in the Product Backlog.
     Your five checks are the third part of Lab 03; write them so that a second person can verify each one.
```

Recap · the five events and the three artifacts on one page

Event	Max time-box (one-month Sprint)	Inspects	Adapts
The Sprint	one month or less, fixed	— (container)	—
Sprint Planning	8 h	Product Backlog (ready items), capacity, Definition of Done	creates the Sprint Backlog: Sprint Goal, items, plan
Daily Scrum	15 min	progress toward the Sprint Goal	the Sprint Backlog — plan for tomorrow
Sprint Review	4 h	the outcome (the Increment), with stakeholders	the Product Backlog
Sprint Retrospective	3 h	individuals, interactions, processes, tools, Definition of Done	the way of working; improvements → next Sprint Backlog
Artifact → commitment		Product Backlog → Product Goal · Sprint Backlog → Sprint Goal	Increment → Definition of Done



Team Studio · 120 minutes · Sprint 1 starts now

- 10 min — Planning — the studio goal on the screen: "Sprint 1 is planned, our board is up, our Definition of Done has five checks." Hats out (facilitator, timekeeper, scribe, presenter).
- 15 min — Product Backlog v1 — 8 to 10 items in plain language, one line each, ordered by this Sprint's Product Owner (user stories come next week).
- 20 min — Sprint Planning — why: the Sprint Goal in one sentence; what: 3 to 5 items within a capacity you choose cautiously; how: work items of two hours or less, written on the board.
- 25 min — Definition of Done workshop — five observable checks that every item of Sprint 1 must pass; written at the top of the board.
- 20 min — Build — start the first work items; hold a real 15-minute Daily Scrum at minute 10 of this block, standing, with the Scrum Master timing it.
- 20 min — Sprint Review rehearsal — each team shows its Sprint Goal and its Definition of Done in 90 seconds; the class gives one suggestion per team.
- 10 min — Retrospective — start / stop / continue on sticky notes, one per person; attendance.

Home Sprint · 120 minutes, and next Monday

- Read: Denning, The Age of Agile, Chapter 4 "The Law of the Network" (in VitalSource Bookshelf); re-read the sections "Scrum Events" and "Scrum Artifacts" of the Scrum Guide 2020 (about five pages).
- Run three asynchronous Daily Scrums during the week (a message thread at a fixed time counts) and log them: date, progress toward the Sprint Goal, impediment, plan adapted — the format of Lesson 2.
- Move the cards on your board as work gets Done; keep the dates — you will need them in Class 6.
- Write your Learning Log (five lines: what I did, what I learned, what surprised me, one question, one thing I will apply next week).
- Next Monday, October 19 — Class 5 and Lab 03 (Sprint 1 Kit & User Story Set): eight items as user stories with a one-line acceptance test · your five checks · your Sprint Goal · points + one forecast · three Daily Scrum lines
- Feedback date Sunday, October 25, 23:59 · final deadline of every lab: Sunday, December 20, 2026, 23:59

Watch at home (1/2) · Lessons 1 and 2 · all under 15 minutes

▶️ Lesson 1 · Sprint Planning Basics - Agile Coach (2019) — Atlassian · 1:31 https://www.youtube.com/watch?v=yvFcRcmrMaU

▶️ Lesson 1 · Sprint Planning Meetings - Agile Coach (2019) — Atlassian · 2:59 https://www.youtube.com/watch?v=9NWbQlRcdh0

▶️ Lesson 1 · Part 14 An Introductory Video Series to Scrum: Sprint Planning — Scrum.org · 5:01 https://www.youtube.com/watch?v=64TFHpzx0Vs

▶️ Lesson 2 · Daily Standups: How to Run Them - Agile Coach (2019) — Atlassian · 4:14 https://www.youtube.com/watch?v=er9gntPjTJU

▶️ Lesson 2 · What is the Daily Scrum? — Scrum.org · 3:42 https://www.youtube.com/watch?v=mdGQeGYyXfQ

▶️ Lesson 2 · Sprint Review Meetings - Agile Coach (2019) — Atlassian · 4:26 https://www.youtube.com/watch?v=InXAS_zRvqQ

▶️ Lesson 2 · What is a Sprint Review 2020 — Scrum.org · 4:46 https://www.youtube.com/watch?v=uYHRRM9foMQ

Watch at home (2/2) · Lessons 3 and 4 · all under 15 minutes

▶️ Lesson 3 · Agile Retrospectives Done Right - Agile Coach (2019) — Atlassian · 5:10 https://www.youtube.com/watch?v=dJNCHvqKljU

▶️ Lesson 3 · Scrum Artifacts - Agile Coach (2018) — Atlassian · 2:12 https://www.youtube.com/watch?v=BkiAMlUF3YI

▶️ Lesson 3 · Part 11 An Introductory Video Series to Scrum: Sprint Backlog and Sprint Goal — Scrum.org · 7:13 https://www.youtube.com/watch?v=EbHC8vzGqEg

▶️ Lesson 4 · Crafting a Definition of Done — Scrum.org · 4:29 https://www.youtube.com/watch?v=2MD5onpE6jg

▶️ Lesson 4 · Part 12 An Introductory Video Series to Scrum: Increment and Definition of Done — Scrum.org · 8:15 https://www.youtube.com/watch?v=DMqJjU0o3rQ

Links · official sites used in this lecture

- The Scrum Guide 2020 — scrumguides.org https://scrumguides.org/scrum-guide.html
- Scrum Guides — home page https://scrumguides.org/
- Scrum Guide revision history — scrumguides.org https://scrumguides.org/revisions.html
- Creative Commons Attribution-ShareAlike 4.0 — creativecommons.org https://creativecommons.org/licenses/by-sa/4.0/
- Scrum.org https://www.scrum.org/
- Scrum.org — "Crafting a Definition of Done" (video page) https://www.scrum.org/resources/crafting-definition-done
- Scrum.org — "What is the Daily Scrum?" (video page) https://www.scrum.org/resources/what-daily-scrum
- Scrum.org — "What is a Sprint Review?" (video page) https://www.scrum.org/resources/what-sprint-review
- Scrum.org — An Introductory Video Series to Scrum https://www.scrum.org/resources/introductory-video-series-scrum
- Atlassian Agile Coach — atlassian.com/agile https://www.atlassian.com/agile
- Atlassian — Sprint Planning guide https://www.atlassian.com/agile/scrum/sprint-planning
- Stephen Denning — stevedenning.com https://www.stevedenning.com/

Links · your course tools, and the Legal Notice

- VitalSource Bookshelf — vitalsource.com https://www.vitalsource.com/
- Blackboard — blackboard.com https://www.blackboard.com/
- tutor.com https://www.tutor.com/
- VirusTotal — link check https://www.virustotal.com/gui/home/url
- Google Safe Browsing — site status https://transparencyreport.google.com/safe-browsing/search
- Cyber.SoHo — Legal Notice, Terms of Use and Acceptable Use Policy (v2.0) https://cyber-soho.github.io/prevmon/00.01.%20cyber.soho%20-%20legal.html



Sprint 1 starts now.

Team Studio: Product Backlog v1 · Sprint Planning · Definition of Done · first Daily Scrum · Review rehearsal · Retrospective

Cyber.SoHo Educational Hub · From the Industry to the Classroom — Building the IT's Future, Today and Together !
Legal Notice, Terms of Use and Acceptable Use Policy: https://cyber-soho.github.io/prevmon/00.01.%20cyber.soho%20-%20legal.html
Scrum Guide 2020 wording © Ken Schwaber and Jeff Sutherland, CC BY-SA 4.0 · Team Menu and its members are fictional
